LAB 2
AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

Coffee Ordering Kiosk System

NAME : Shweta Mailaragouda Patil

SRN : PES2UG25CS825

1. Objective

Use Jira to convert the functional requirements of the Coffee Ordering Kiosk System into Agile backlog items, estimate and prioritize the work, simulate sprint progress, and analyse the sprint using a Burndown Chart.

2. Jira Project / Space Setup

A Jira space named “Coffee Ordering Kiosk 2” was created using the Scrum template. The space uses the COK2 key and was configured for the Agile/Scrum workflow.

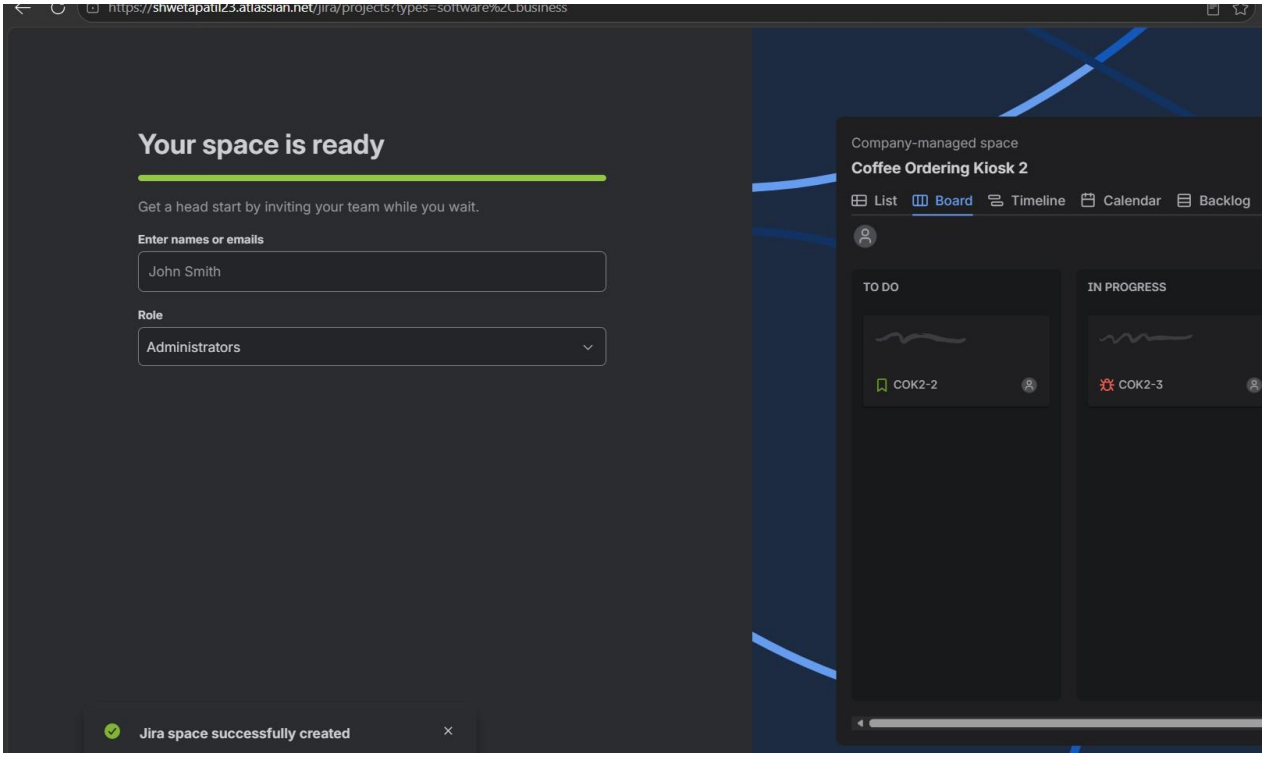


Figure 1. Jira space successfully created – Coffee Ordering Kiosk 2.

3. Backlog Creation and Estimation

The backlog contains the coffee-ordering user stories with story-point estimates and priorities. The visible stories include Coffee Selection (3 points), Size Selection (2 points), Customize Coffee (5 points), Payment (5 points), and Order Confirmation (3 points).

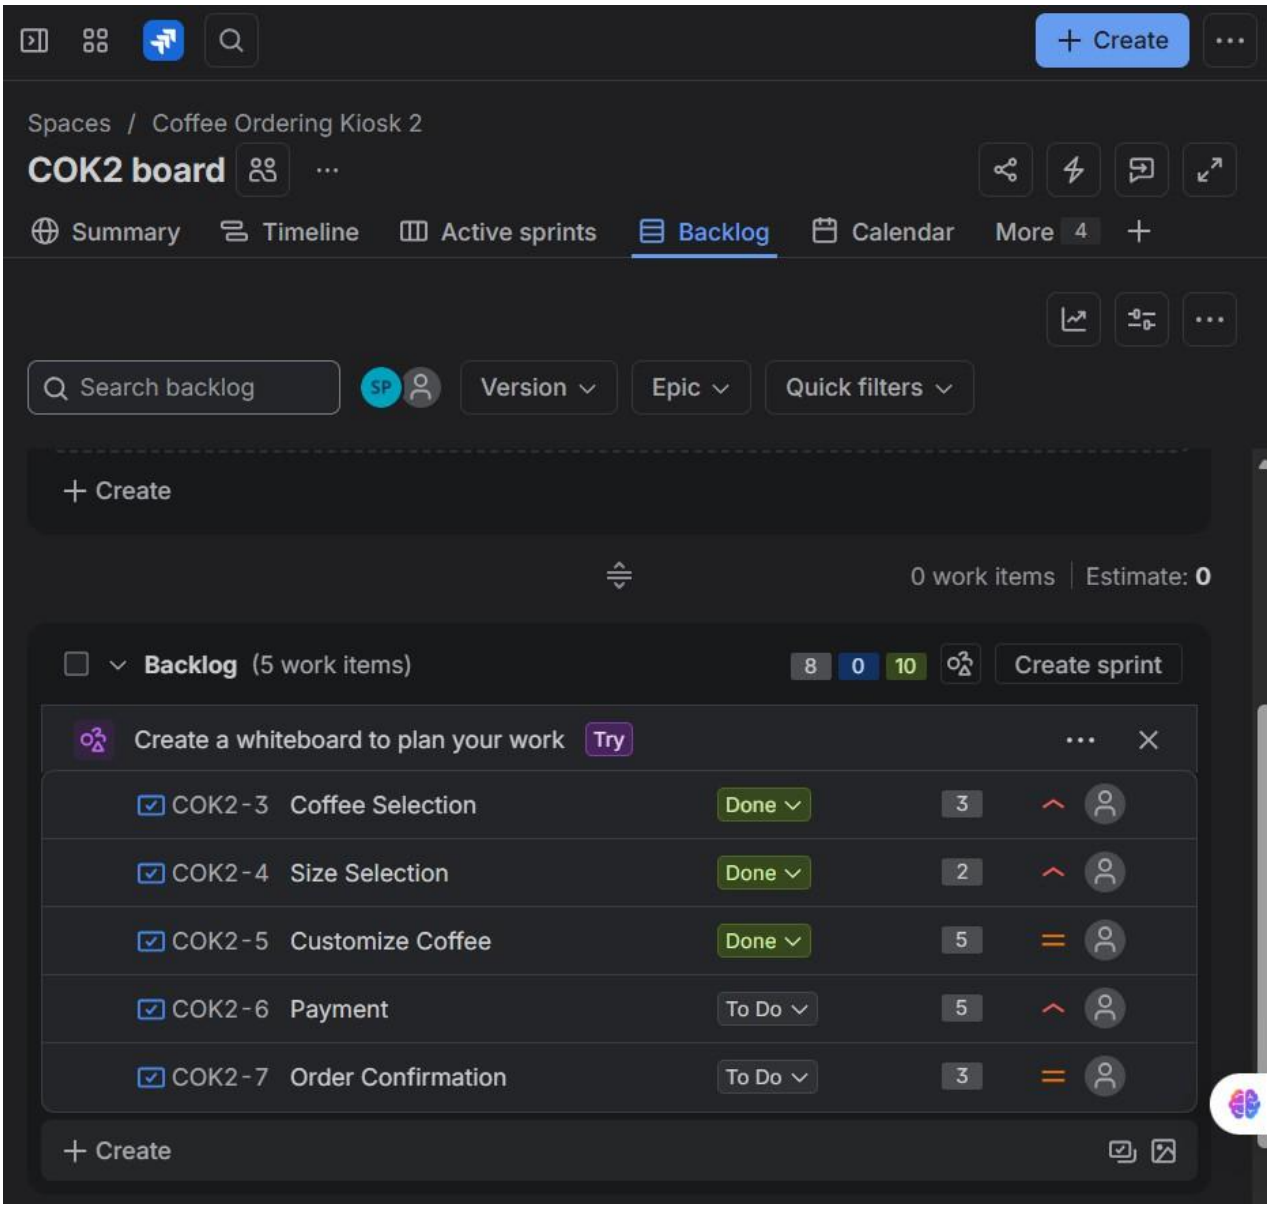


Figure 2. Jira backlog showing the Coffee Ordering Kiosk user stories, story points, and statuses.

4. Sprint Planning

The selected work was moved into a sprint for simulation. Sprint 2 contains three stories: Coffee Selection (3 points), Size Selection (2 points), and Customize Coffee (5 points), giving a total estimate of 10 story points.

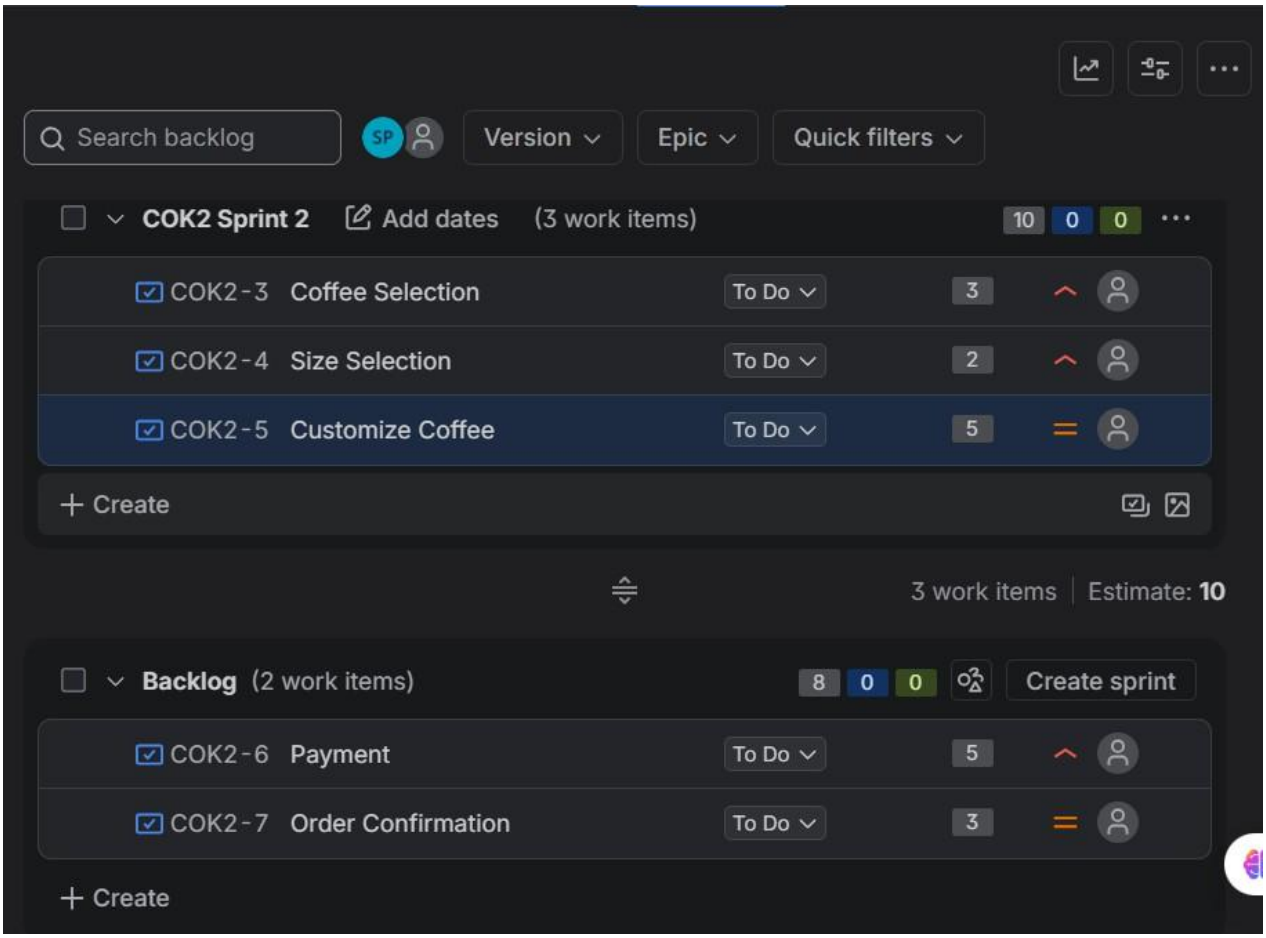


Figure 3. Sprint 2 containing three selected stories with a total estimate of 10 story points.

5. Sprint Simulation / Progress

The sprint was simulated by changing work-item status through the Scrum workflow. The completed stories appear in the Done column, demonstrating progress from To Do towards completion.

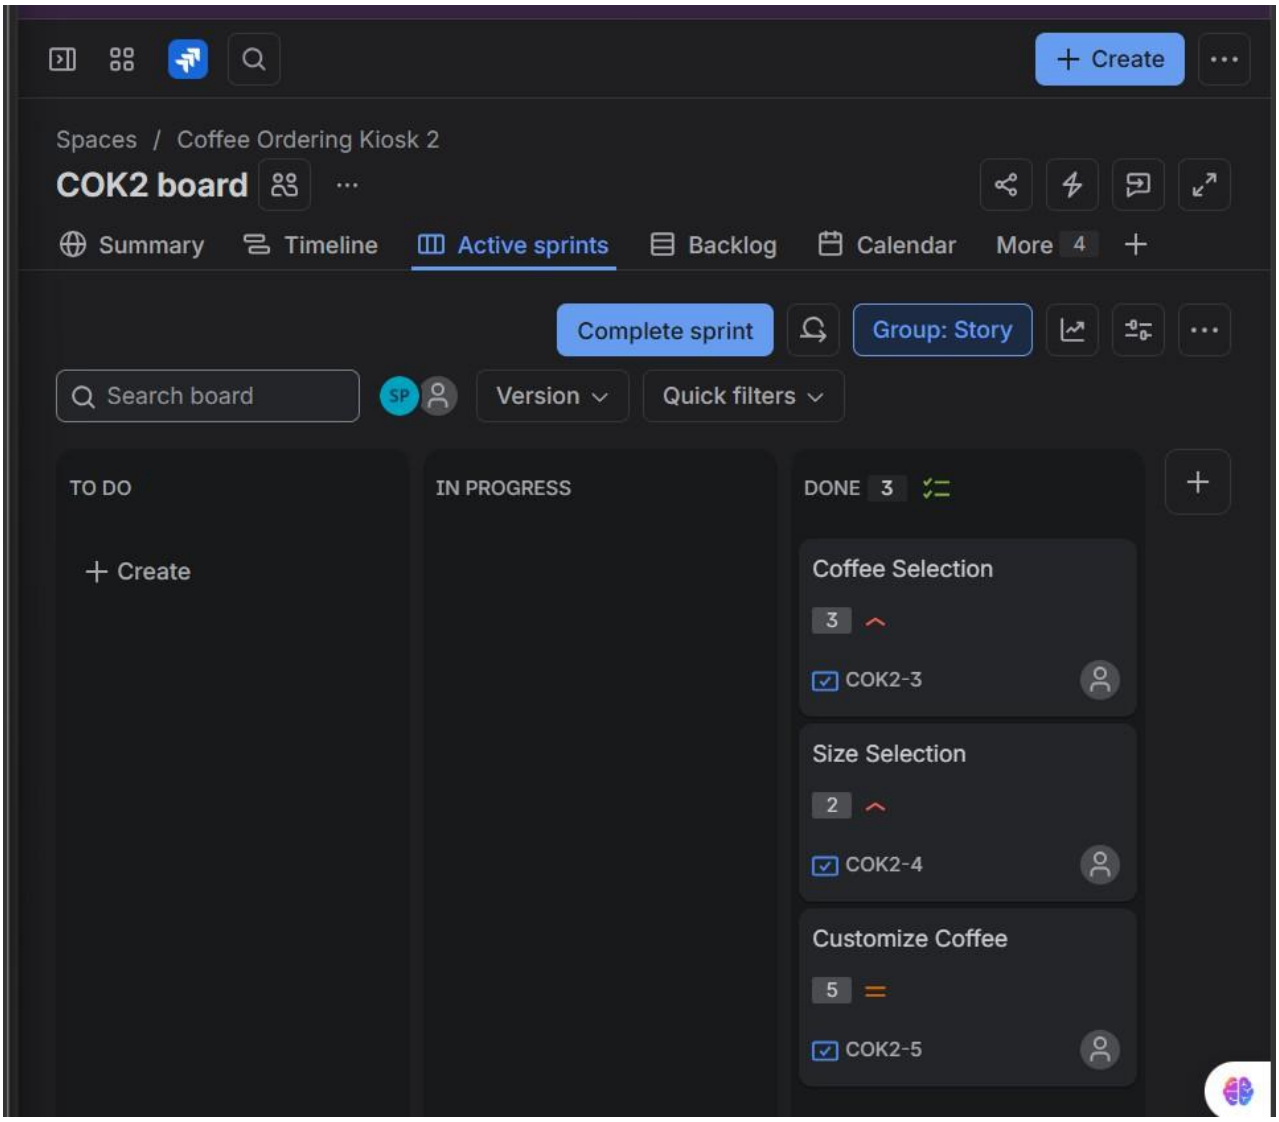


Figure 4. Active Sprint board showing sprint work and completed items.

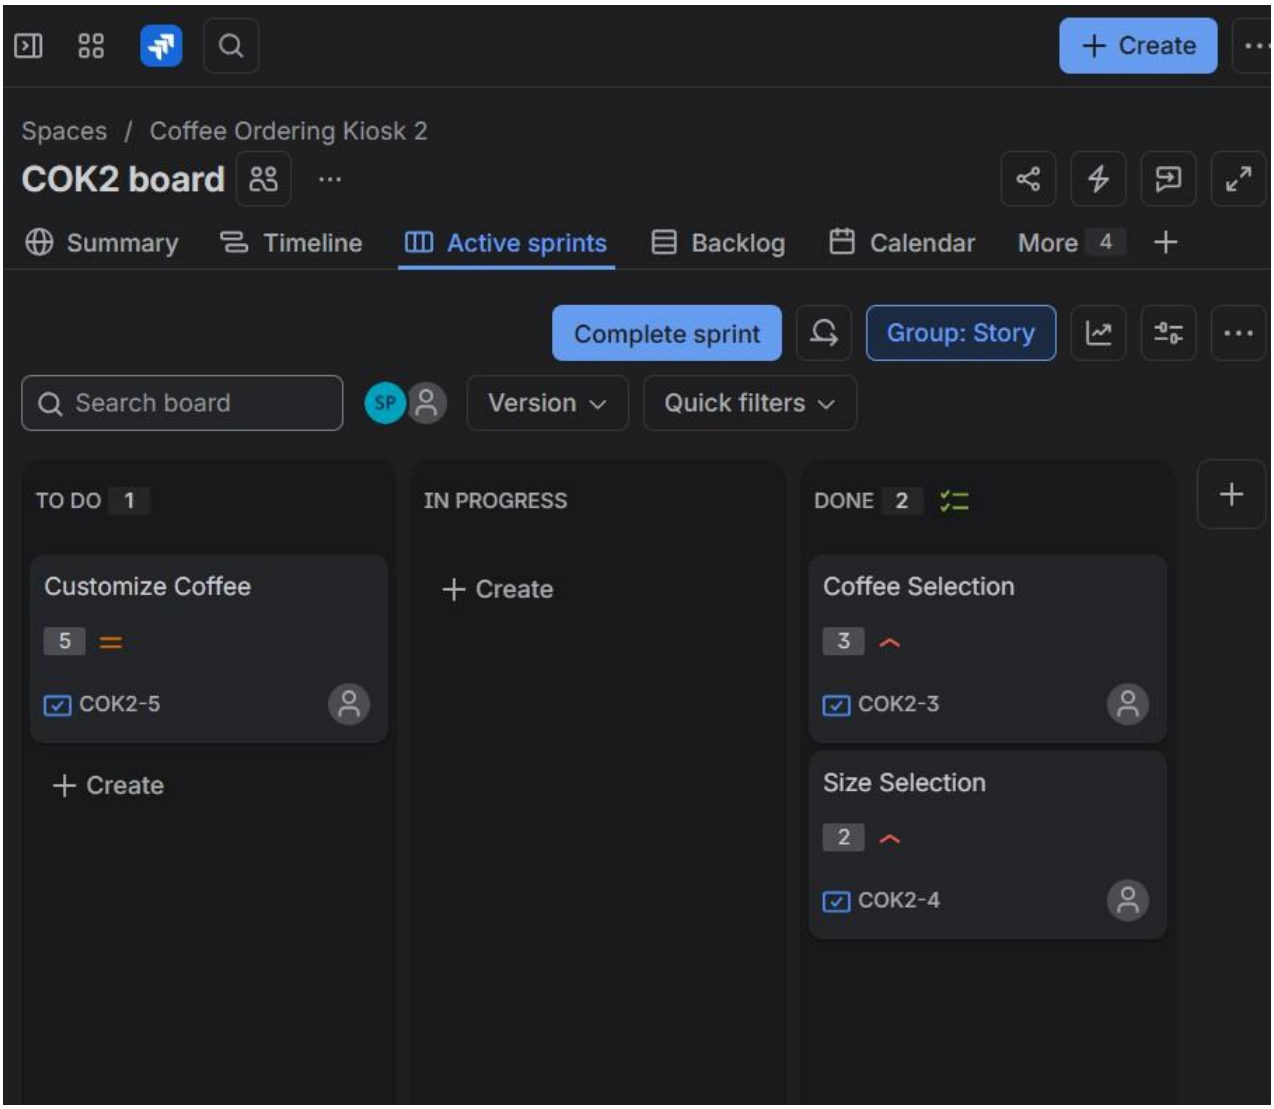


Figure 5. Active Sprint board after moving the selected stories to Done.

6. Burndown Chart

The Burndown Chart was opened from Jira Reports. It displays the sprint using Story Points and shows the remaining work against the guideline for expected progress.

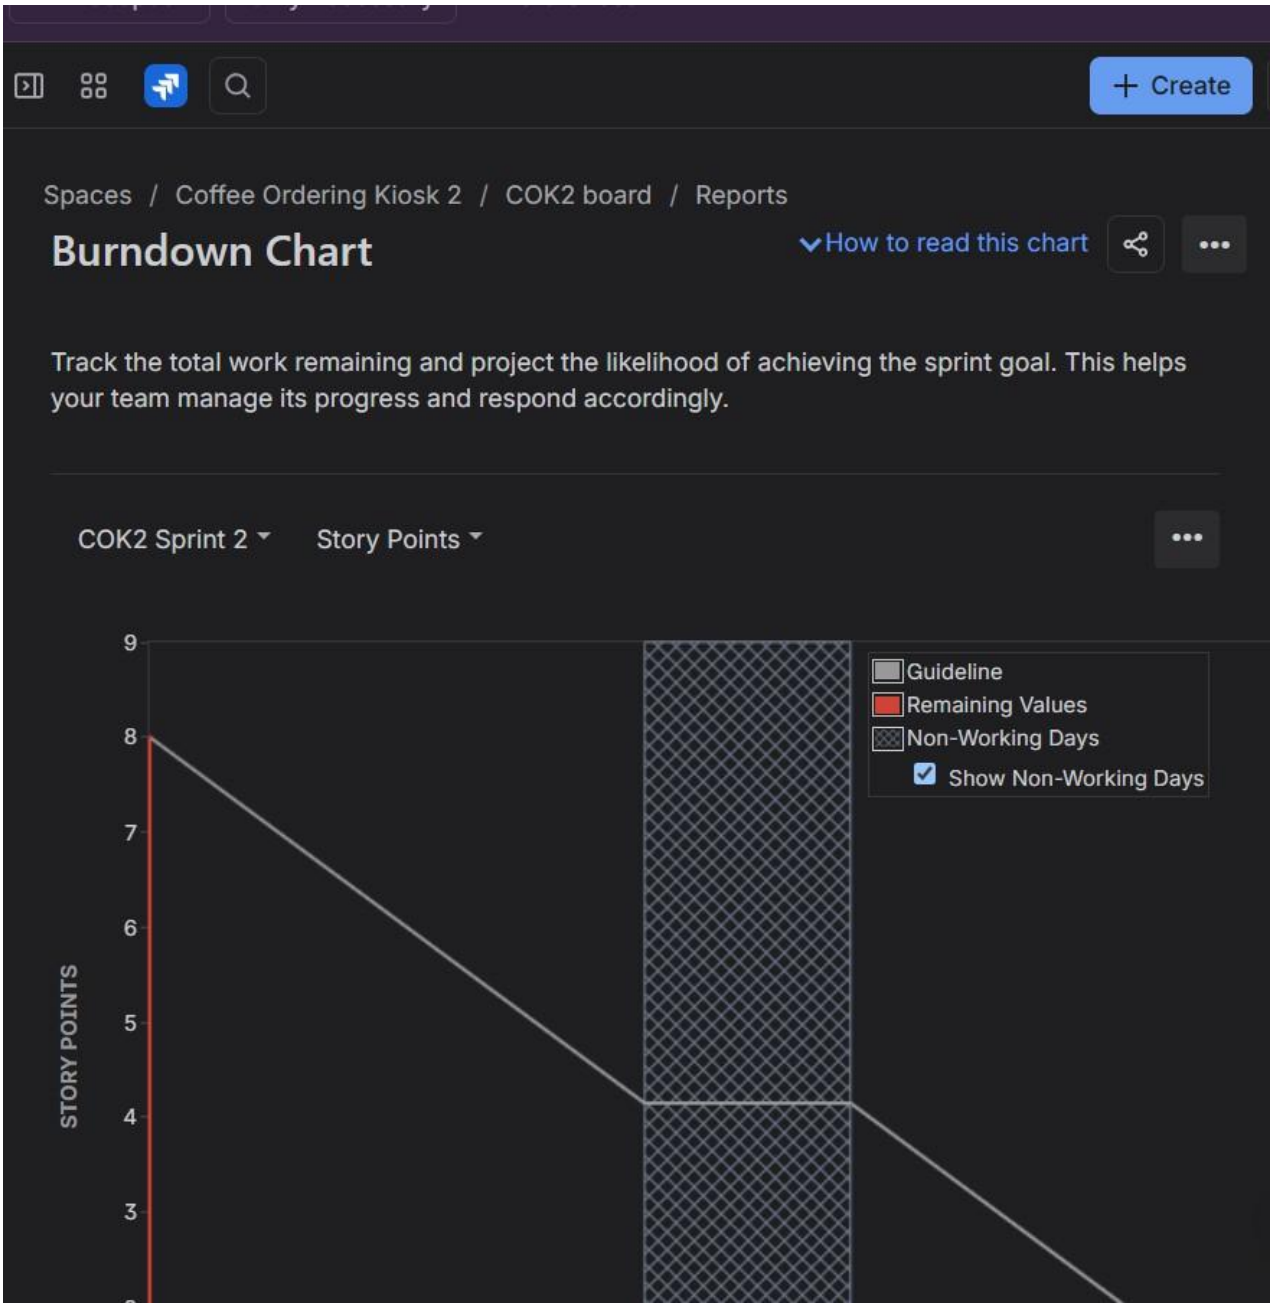


Figure 6. COK2 Sprint 2 Burndown Chart using Story Points.

				Story Points		
Date	Issue	Event Type	Event Detail	Inc.	Dec.	Remaining
30/Aug/26 9:59 PM	COK2-6	Sprint start		5		
	COK2-7			3		
	Total					8
30/Aug/26 10:00 PM	COK2-6	Burndown	Issue completed		5	3
	COK2-7	Burndown	Issue completed		3	0
30/Aug/26 10:01 PM	COK2-6	Sprint ended by Shweta Patil				0
	COK2-7					0
	Total					0

7. Reflection Questions

1. Did your estimations reflect the actual effort?

Yes. The story-point estimates gave a reasonable representation of the effort required. Some tasks required more effort than others but the estimates were useful for planning the sprint.

2. Was your backlog well-prioritized?

Yes. The backlog was prioritized according to the importance and sequence of the coffee-ordering process. Essential features were handled first, followed by payment and order confirmation.

3. How did your simulated sprint align with your plan?

The simulated sprint generally aligned with the plan. The selected user stories were completed by progressing them through the Scrum workflow from To Do to In Progress and then to Done.

4. What insights did the burndown chart give about your team’s capacity?

The burndown chart showed how the remaining story points changed during the sprint. It provided a visual indication of progress and helped assess whether the team's work was progressing at the planned pace.

8. Conclusion

The Coffee Ordering Kiosk backlog was created and managed in Jira using Agile/Scrum practices. The sprint was planned and simulated, work items were progressed to completion, and the Burndown Chart was used to analyse sprint progress and team capacity.
